

#396 - 301 Dishwasher


Completed with Issues | Andy Chang | Cabinetry
Plan: Level 3
Created 05-06-2026



Task messages (time in PDT)

Installer IQIS	Photo 1 - GPS: 49.2320689, -123.1849556	07 May 11:49 AM
Installer IQIS	Ritish- Plumbing pipe is in the way of dishwasher as this needs to be done first before inst allation	07 May 11:50 AM
Installer IQIS	Jt:- they fix it	07 May 01:21 PM
Installer IQIS	Photo 2	07 May 01:21 PM
Installer IQIS	Photo 3	07 May 01:21 PM
Installer IQIS	Photo 4 - GPS: 49.2340826, -123.1941545	07 May 01:22 PM
Installer IQIS	Photo 5 - GPS: 49.2340826, -123.1941545	07 May 01:22 PM
Installer IQIS	Photo 6 - GPS: 49.2340847, -123.1941595	07 May 01:22 PM
Installer IQIS	Jt:- its level, site guy says ok install after it sticking out coz of that back pipe in the way.	07 May 01:23 PM
Installer IQIS	Jt:- Gabel is not leveled.	07 May 01:23 PM

Photos

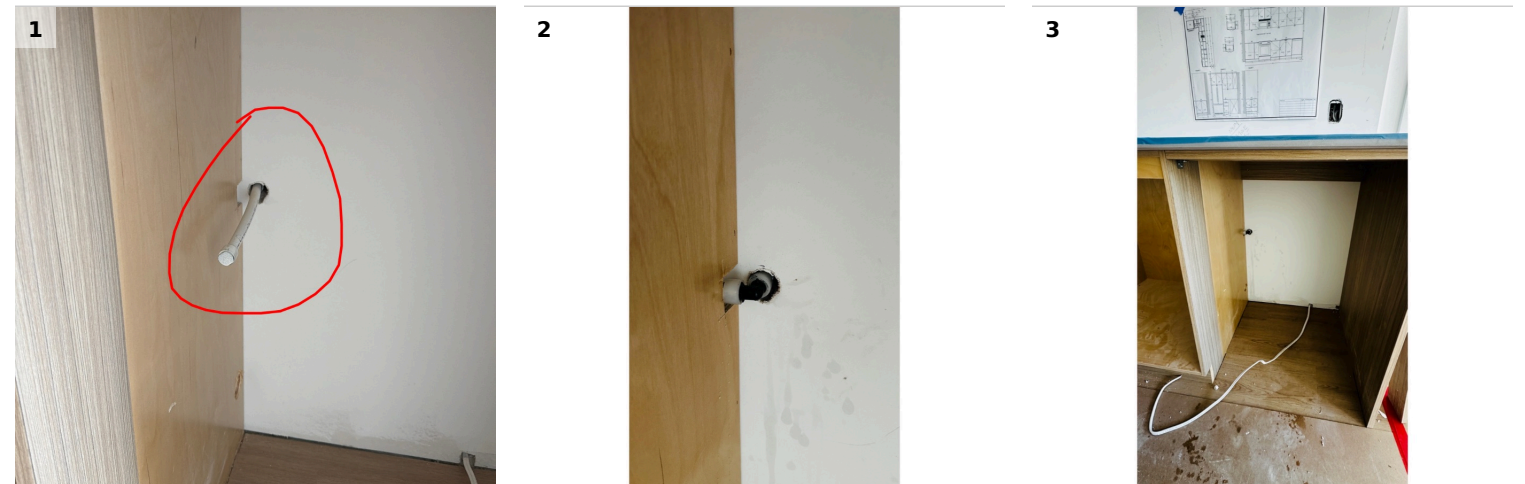

4



5



6

